

**CONSTRUCTION &
ENVIRONMENTAL
MANAGEMENT PLAN FOR A
RESIDENTIAL
DEVELOPMENT
AT
MOUNTGORRY, SWORDS
MALAHIDE ROAD, SWORDS,
CO. DUBLIN**

The Tecpro Building,
Clonshaugh Business & Technology Park,
Dublin 17, Ireland.

T: + 353 1 847 4220
F: + 353 1 847 4257
E: info@awnconsulting.com
W: www.awnconsulting.com

Report Prepared For

Bartra Propco 23 Limited

Report Prepared By

Brian Maguire, Environmental Consultant
&
Chonaiil Bradley, Principal
Environmental Consultant

Our Reference

BM/237501.0143WMR02

Date of Issue

24 September 2024



Document History

Document Reference		Original Issue Date	
BM/237501.0143WMR02		24 September 2024	
Revision Level	Revision Date	Description	Sections Affected

Record of Approval

Details	Written by	Approved by
Signature	Brian Maguire	
Name	Brian Maguire	Chonaiil Bradley
Title	Environmental Consultant	Principal Environmental Consultant
Date	24 September 2024	24 September 2024

CONTENTS		Page
1.0	INTRODUCTION	4
2.0	DESCRIPTION OF THE PROJECT	4
3.0	CONSTRUCTION PROGRAMME AND PHASING	6
3.1	Excavation & Construction Phase	7
4.0	EXCAVATIONS	8
4.1	Archaeological and Architectural Heritage	8
4.2	Ground Conditions	8
5.0	SITE LOGISTICS	8
5.1	Site Safety Compliance	8
5.2	Site Establishment and Security	9
5.3	Consents and Licenses	9
5.4	Services and Utilities	9
5.5	Material Handling and Storage	10
5.6	Visitor Management	10
5.7	Site Working Hours	10
5.8	Employment and Management Workforce	10
6.0	CONSTRUCTION TRAFFIC AND SITE ACCESS	11
6.1	Traffic Queueing	11
6.2	Site Hoarding and Security Fencing	11
7.0	SAFETY, HEALTH AND ENVIRONMENTAL CONSIDERATIONS DURING CONSTRUCTION WORKS	12
7.1	Construction Lighting	12
7.2	Air Quality	12
7.3	Ecology	15
7.4	Noise and Vibration	15
7.5	Resource and Waste Management	19
7.6	Surface Water Management	21
8.0	SUMMARY	22
9.0	REFERENCES	23

1.0 INTRODUCTION

This Construction Environmental Management Plan (CEMP) has been prepared by AWN Consulting (AWN) on behalf of Bartra Propco 23 Limited. Bartra Propco 23 Limited intend to apply for permission for development of a Large-scale Residential Development (LRD) at this site fronting the Swords to Malahide Road (R106), Mountgorry, Swords, Co. Dublin. The proposed development will principally provide 123 No. residential units (55 No. one bed apartments and 68 No. two bed apartments) in a courtyard block arrangement ranging in height from part 4 No. to part 5 No. storeys. The development also includes ancillary residential amenities, 24 No. car parking spaces, vehicular and pedestrian access points, a connection to the parcel of existing public open space west of the site and public and communal open spaces.

This CEMP explains the construction techniques and methodologies which will be implemented during construction of the proposed development.

The CEMP mitigation measures will be implemented to ensure that pollution and nuisances arising from site clearance and construction activities is prevented where possible and managed in accordance with best practice environmental protection.

The CEMP will be implemented and adhered to by the construction Contractor and will be overseen and updated as required if site conditions change by the Project Manager, Environmental Manager and Resource Manager where relevant. All personnel working on the site will be trained in the implementation of the procedures.

This CEMP has been prepared to account for activities at the site during the excavation and construction phase of the project.

The main issues that have been considered within this document are as follows;

- Description of works;
- Construction programme and phasing;
- Site logistics;
- Workforce;
- Public relations and community liaison;
- Construction traffic and access; and
- Safety, health and environmental management.

2.0 DESCRIPTION OF THE PROJECT

Bartra Propco 23 Limited intend to apply for permission for development for a Large-scale Residential Development (LRD) at this c. 0.8731 Ha site fronting the Swords to Malahide Road (R106), Mountgorry, Swords, Co. Dublin. The site is bounded to the west by open space, with Seamount View Housing Estate further beyond, to the south by the R106, to the east by an access road to the Applegreen Service Station and to the north by Swords Business Park.

The development's surface water drainage network shall discharge from the site into the respective existing manhole located along the access road to the east of the site. The development site area and drainage work areas will provide a total application site area of c. 0.8792 Ha.

The proposed development will principally consist of: the construction of 123 No. residential units (55 No. one bed apartments and 68 No. two bed apartments). The development will be provided in a courtyard block arrangement ranging in height from

part 4 No. to part 5 No. storeys. The proposed development has a gross floor area of c. 10,281 sq m.

The proposed development will also provide: vehicular access from the access road to the east; 24 No. car parking spaces; bicycle parking spaces; motorcycle parking spaces; pedestrian/cycle entrances at the south-west and north of the site, and along the western boundary connecting into the adjoining open space; a footpath and bicycle path around the south, east and north of the site perimeter and a shared cycle/pedestrian path along the western boundary; balconies and terraces facing all directions; hard and soft landscaping; boundary treatments; green roofs; lift overrun; PV panels; lighting; ESB substation; switchroom; plant; and all associated works above and below ground.

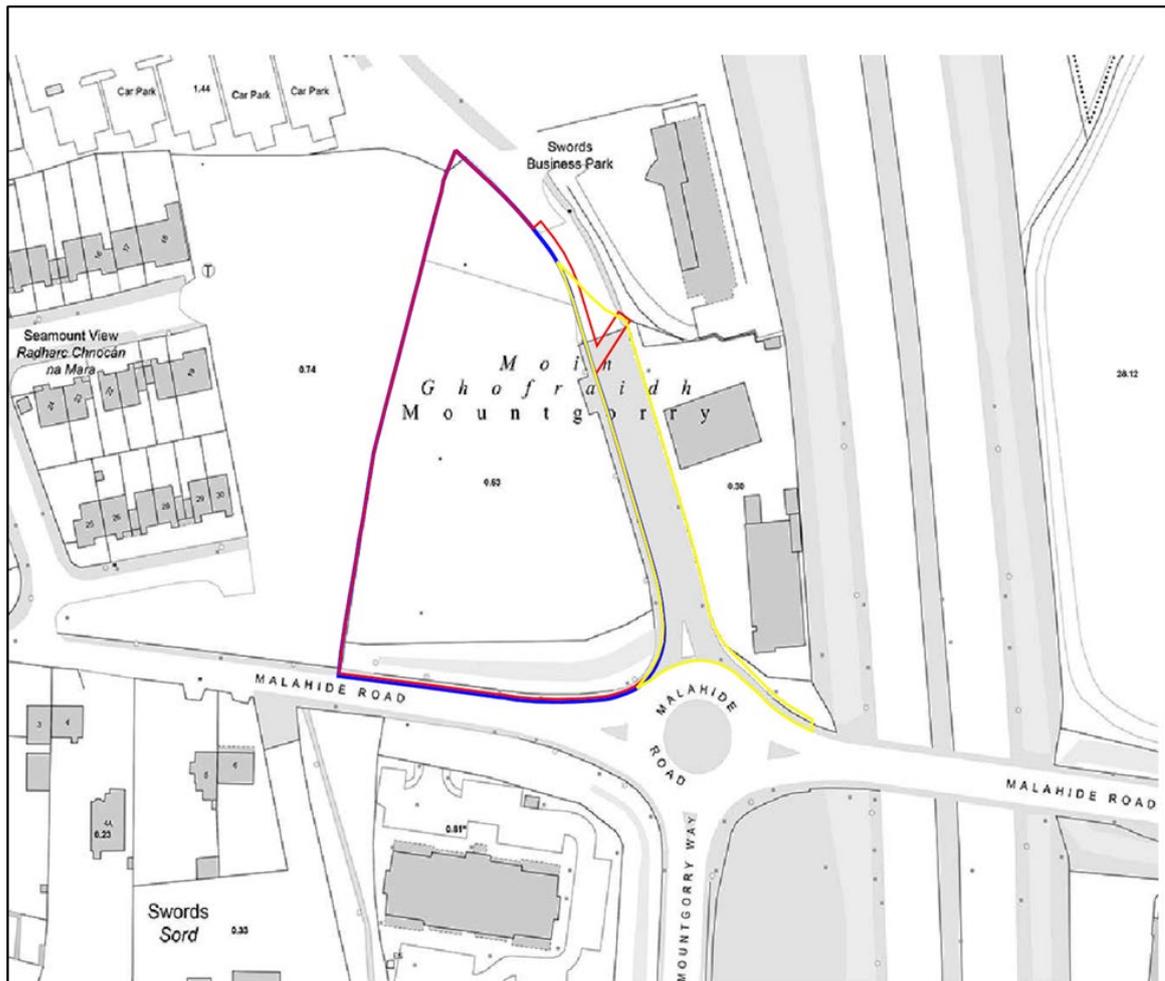


Figure 2.1 Site Location Map

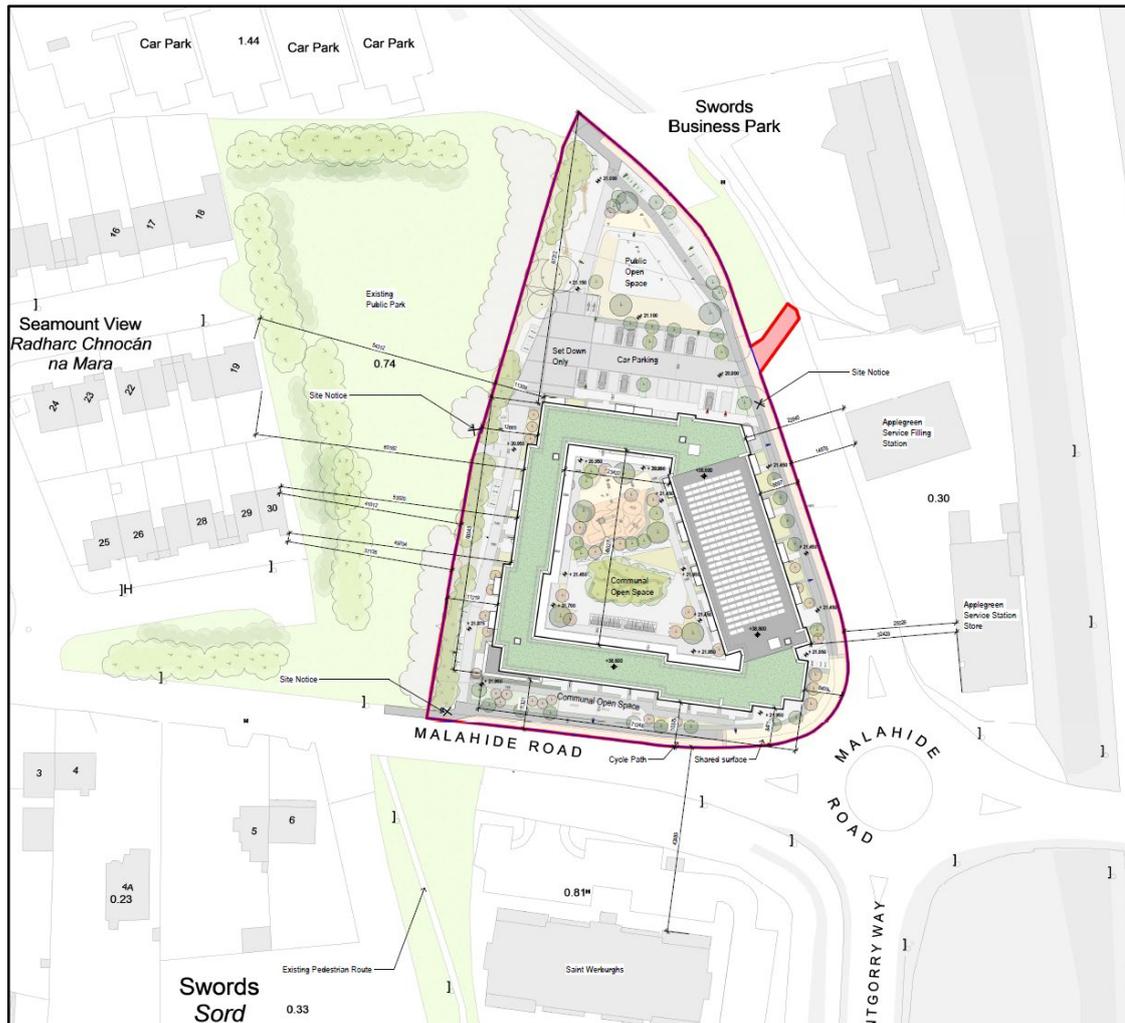


Figure 2.2 Site Layout Map

3.0 CONSTRUCTION PROGRAMME AND PHASING

The construction works associated with the development will be undertaken in a single phase. The Construction work is expected to take approximately 24 months for the earthworks and construction phase prior to commencement of full operations and occupation.

It is currently envisaged that the construction compound, offices, staff parking and storage areas will be located at the position indicated in Figure 3.1.



Figure 3.1 Potential Location for Site Compounds and Storage

3.1 Excavation & Construction Phase

The project excavations will involve excavations for new foundations, site levelling and excavations for roads and services. The Resource Waste Management Plan prepared by AWN Consulting Ltd (237501.0143WMR01) for the development will be updated by the main contractor and will be in compliance with the requirements of the *'Best Practice Guidelines for the Preparation of Resource & Waste Management Plans for Construction & Demolition Projects'* published by the Environmental Protection Agency (November 2021)¹, which will identify and categorise any waste arising from the development.

The plan contains the proposals for the minimisation, re-use and re-cycling of site generated waste. As part of this plan separate storage areas will be designated on the site for various types of material in order to maximise the re-use and re-cycling potential. Procedure will also be put in place to ensure that all sub-contractors fulfil the requirements of the Waste Management Plan.

The project involves the construction of residential apartments comprising of 124 No. residential units (55 No. one bed apartments and 69 No. two bed apartments) in a courtyard block arrangement ranging in height from part 4 No. to part 5 No. storeys.

The works will include:

- Site set up, welfare facilities and compound establishment, decommissioning and movement of site compound and facilities as needed.
- Set up of hoarding around compound and the site boundary.
- Erection of safety signage to all areas and implementation of traffic/pedestrian management plan.

4.0 EXCAVATIONS

4.1 Archaeological and Architectural Heritage

Should archaeological features or material be uncovered during archaeological testing or any phase of construction, ground works will cease immediately and the National Monuments Service of the Department of Housing, Local Government and Heritage will be informed. Time must be allowed for a suitably qualified archaeologist to inspect and assess any material. If it is established that archaeologically significant material is present, the National Monuments Service may require that further archaeological mitigation be undertaken.

4.2 Ground Conditions

In the event that contaminated material is found on site, this material will need to be segregated from clean/inert material, tested and classified as either non-hazardous or hazardous in accordance with the EPA publication entitled '*Waste Classification: List of Waste & Determining if Waste is Hazardous or Non-Hazardous*'² using the *HazWasteOnline* application (or similar approved classification method). The material will then need to be classified as clean, inert, non-hazardous or hazardous in accordance with the *EC Council Decision 2003/33/EC*³, which establishes the criteria for the acceptance of waste at landfills.

In the event that Asbestos Containing Materials (ACMs) are found, the removal will only be carried out by a suitably permitted waste contractor, in accordance with *S.I. No. 386 of 2006 Safety, Health and Welfare at Work (Exposure to Asbestos) Regulations 2006-2010*. All asbestos will be taken to a suitably licensed or permitted facility.

In the event that hazardous soil, or historically deposited waste is encountered during the construction phase, the contractor will notify Fingal County Council (FCC) and provide a Hazardous/Contaminated Soil Management Plan, to include estimated tonnages, description of location, any relevant mitigation, destination for disposal/treatment, in addition to information on the authorised waste collector(s).

5.0 SITE LOGISTICS

5.1 Site Safety Compliance

The Contractor shall be responsible for overall management of the site for the duration of the proposed works and will progress their works with reasonable skill, care, diligence and to proactively manage the works in a manner most likely to ensure the safety and welfare of those carrying out construction works.

The Contractor shall comply with all relevant Statutory requirements such as the 2005 Safety Health and Welfare at Work Act, The Construction Regulations (SI 291 of 2013), the General Application Regulations (SI 299 of 2007), etc. (and any amendments thereof).

In addition, the Contractor shall comply with all the reasonable safety requirements of the Client, the Project Supervisor for the Design Process and the Project Supervisor for the Construction Stage.

5.2 Site Establishment and Security

The first activity to be carried out at the site will be the establishment of site facilities and security. It is anticipated that site establishment works will take approximately two weeks. The site office and welfare facilities will be confirmed in advance of the commencement of site works and agreed with FCC. Figure 3.1 shows the potential locations of the site compound and staff parking.

All of the sub-contractors as well as the main contractor and project managers will occupy offices within the construction compounds. The site parking for all staff, contractors and visitors will also be located in this area. Carpooling and the use of public transport will be encouraged to reduce pressure on parking in the area.

5.3 Consents and Licenses

All statutory consents and licences required to commence on-site construction activities will be obtained ahead of works commencing, allowing for the appropriate notice period. These will include, but are not limited to:

- Site notices;
- Construction commencement notices; and
- Licence to connect to existing utilities and mains sewers, where required;

5.4 Services and Utilities

Welfare facilities (canteens, toilets etc.) will be available within the construction compound and this will remain in place for the construction of the proposed development. The offices and site amenities will initially need to have their own power supply (generator), water deliveries and foul water collection until connections are made to the mains networks.

Electrical connections will be made by suitably qualified personnel following consultation with the relevant authorities and will be cognisant of subsequent construction works. High voltage connections will be established for heavy duty equipment and site facilities, as required.

The current electricity facilities on the site of the proposed development are supplied by the ESB through a ring network. All electrical works, including connection to the ESB network will be carried out by a suitably qualified contractor.

Water supply required for welfare facilities, dust suppression and general construction activities will be sourced from the existing public piped supplies running into the site.

Although before connections are established to the water supply it may need to be trucked onto site. As with electrical works, this will be carried out by a suitably qualified contractor. It will be necessary to service the site with a reliable and safe water supply.

Site welfare facilities will be established to provide sanitary facilities for construction workers on site. The main contractor will ensure that sufficient facilities are available at all times to accommodate the number of employees on site. Foul water from the offices and welfare facilities on the site will discharge into the existing sewer on site (the cabins may initially need to have the foul water collected by a licensed waste sewerage contractor before connection to the sewer line can be made).

5.5 Material Handling and Storage

Key materials which will be ordered by specific order for the project, a 'Just in Time' delivery system will operate to minimise storage of materials, the quantities of which are unknown at this stage.

Where possible it is proposed to source general construction materials from the Dublin area to minimise transportation distances.

Aggregate materials such as sands and gravels will be stored in clearly marked receptacles in the compound area within the site. Liquid materials will be stored within temporary bunded areas, doubled skinned tanks or bunded containers (all bunds will conform to standard bunding specifications – BS EN 1992-3:2006⁴) to prevent spillage.

Construction materials will be brought to site by road. Construction materials will be transported in clean vehicles. Lorries/trucks will be properly enclosed or covered during transportation of friable construction materials and spoil to prevent the escape material along the public roadway.

The majority of construction waste materials generated will be soil from excavation works. Material will be removed from site regularly to ensure there is minimal need for stockpiling.

5.6 Visitor Management

Visitors will only be allowed to enter the main site compound via the designated pedestrian access gate. A dedicated, secured footpath to the site office is established at the gate for registration and obtaining PPE prior to entering the site. A log will be maintained by security to control access to the site. Visitors will be required to attend a site-specific induction to allow access to the compound and/or construction site unless being accompanied by an inducted member of the site team.

Visitors will then be taken by an inducted member of the construction team to the required area of the site.

5.7 Site Working Hours

Site development and building works will only be carried out between the hours of 0700 to 1900 Mondays to Fridays inclusive and between 0800 and 1400 hours on Saturdays. There will be no construction works carried out on Sundays or public holidays. Deviation from these times will only take place when written approval is granted by FCC in exceptional circumstances.

5.8 Employment and Management Workforce

It is estimated that there will initially be 45-60 staff on site on a typical day, however during peak construction periods this is expected to fluctuate up to 80 staff and contractors on site per day.

It is anticipated that the key project managers and main contractor representatives will maintain a presence on site for the whole duration of the project and the labour workforce will be determined by the specialist contractors required on site.

All employees working on the site will be required to have a SafePass Card (or similar approved Construction Health & Safety card), manual handling training, CIF COVID 19 training and the necessary certificates to operate machinery as required. The details

of training required, records maintained, and induction procedures will be outlined in the Main Contractor's Health and Safety Plan(s).

6.0 CONSTRUCTION TRAFFIC AND SITE ACCESS

The proposed construction vehicle routes for the site will require a traffic management plan to be agreed upon with FCC and TII prior to site workings beginning. A Construction Stage Traffic Plan will be prepared post-planning. Advanced warning signs will be placed at sufficient distances to taper off the entry and exit points. Pedestrian marshals will be used as and when required.

The traffic plan will be such that it will minimise the interaction between the construction site and the local residential areas.

Traffic management will be undertaken for the site works in accordance with the principles outlined below and shall comply at all times with the requirements of:

- Department of Transport Traffic Signs Manual 2010 – Chapter 8 Temporary Traffic Measures and Signs for Roadworks ⁵
- Department of Transport Guidance for the Control and Management of Traffic at Road Works (2010) ⁶
- Any additional requirements detailed in Design Manual for Urban Roads & Streets (DMURS) ⁷

Construction traffic operation would be limited to 0700 to 1800 from Monday to Friday and 0800 to 1400 on Saturday for the off-road construction. These times may vary to facilitate specific site requirements and/or construction activities associated with the site. Any variation will be discussed and agreed in advance with FCC.

It should be noted that construction traffic generated during the Construction Phase tends to be outside of peak hours. All construction activities will be agreed with FCC's Roads Department prior to the commencement of the Construction Phase.

In general, the impact of the construction period will be temporary in nature. HGV vehicle movements per hour during the busiest period of construction works are estimated at a peak of 5 HGVs per hour arriving and leaving, but the exact figure will be confirmed by the contractor.

Excavated material will be reused as part of the site development works where possible to minimise truck movements to and from the site (e.g. use as non-structural fill under green areas).

6.1 Traffic Queueing

Material deliveries and collections from site will be planned, scheduled and staggered to avoid any unnecessary build-up of construction works related traffic.

Deliveries to site shall be booked in advance using a delivery schedule, so as to prevent lorry congestion on the road networks surrounding the site. Alternative safe routeways shall be established for traffic and pedestrians where existing routeways have to be altered, removed or worked on during the project.

6.2 Site Hoarding and Security Fencing

All areas of construction will be fenced / hoarded off to prevent unauthorized access. This fencing shall remain closed at all times during construction works and closed and locked after construction work hours / break times.

This fencing shall be erected in accordance with good practice and the Construction Regulations 2013. Fencing arrangements shall be reviewed as the life of the project progresses.

7.0 SAFETY, HEALTH AND ENVIRONMENTAL CONSIDERATIONS DURING CONSTRUCTION WORKS

The appointed main contractor will implement a Construction, Health and Safety Plan during the life of the project, which contains health and safety measures covering the below items at a minimum:

- Construction Health & Safety training requirements;
- COVID-19 guidelines;
- Induction procedures;
- Emergency protocols; and
- Details of welfare facilities.

7.1 Construction Lighting

Construction work will generally be confined to daylight hours and lighting will generally not be required for the construction phase. There will however be occasions where the provision of portable lighting will be required (works on roadways and power floating floors as examples). Where possible and without jeopardising site safety lights will be pointed down at a 45-degree angle and away from sensitive receptors. The site compound will have external lights for safety and security. These lights will be pointed down at a 45-degree angle and away from sensitive receptors where possible.

7.2 Air Quality

This section describes the site policy with regard to dust management and the specific mitigation measures which will be put in place during construction works. The objective of dust control at the site is to ensure that no significant nuisance occurs at nearby sensitive receptors. In order to develop a workable and transparent dust control strategy, the measures set out below have been formulated by drawing on best practice guidance from Ireland, the UK and the US, such as:

- Department of Environment, Heritage and Local Government (DOEHLG), *Quarries and Ancillary Activities, Guidelines for Planning Authorities* (2004) ⁸;
- US Environment Protection Agency (USEPA), *Compilation of Air Pollutant Emission Factors, AP-42, Fifth Edition* (periodically updated) (1986) ⁹;
- The Scottish Office – Development Department, *Planning Advice Note PAN50 Controlling the Environmental Effects Of Surface Mineral Workings Annex B: The Control of Dust at Surface Mineral Workings* (1996) ¹⁰; and
- Institute of Air Quality Management (IAQM), *Guidance on the Assessment of Dust from Demolition and Construction* (2014) ¹¹.

7.2.1 Site Management

The site activities will be undertaken with due consideration of the surrounding environment and the close proximity of sensitive receptors such as residents and pedestrians. Dust management during the construction phase will be the most important aspect in terms of minimising the impacts of the project on the surrounding air quality. The following measures will also be implemented to ensure impacts are minimised:

- Complaint registers will be kept detailing all telephone calls and letters of complaint received in connection with construction activities, together with details of any remedial actions carried out;
- Equipment and vehicles used on site will be in good condition such that emissions from diesel engines etc. are not excessive; and
- Pre-start checks will be carried out on equipment to ensure they are operating efficiently and that emission controls installed as part of the equipment are functional.

Dust deposition levels will be monitored, if requested by the local authority or if complaints are received, to assess the impact that site activities may have on the local ambient air quality. If requested the following procedure will be implemented:

- The dust deposition rate will be measured by positioning Bergerhoff Dust Deposit Gauges at strategic locations near the boundaries of the site for a period of 30 (+/- 2) days if required. Monitoring should be conducted as required during periods when the highest levels of dust are expected to be generated i.e., during site preparation works and soil stripping activities.
- The exact locations will be determined after consideration of the requirements of Method VDI 2119 with respect to the location of the samplers relative to obstructions, height above ground and sample collection and analysis procedures.
- After each 30 (+/- 2 days) exposure period, the gauges will be removed from the sampling location, sealed and the dust deposits in each gauge will be determined gravimetrically by an accredited laboratory and expressed as a dust deposition rate in mg/m²/day in accordance with the relevant standards.
- Technical monitoring reports detailing all measurement results, methodologies and assessment of results shall be subsequently prepared and maintained by the Site Manager.

A limit value of 350 mg/m²/day will be used in comparison with recorded values.

7.2.2 Dust Control Measures

The aim is to ensure good site management by avoiding dust becoming airborne at source. This will be done through good design, planning and effective control strategies. The siting of construction activities and the limiting of stockpiling will take note of the location of sensitive receptors and prevailing wind directions in order to minimise the potential for significant dust nuisance. In addition, good site management will include the ability to respond to adverse weather conditions by either restricting operations on-site or using effective control measures quickly before the potential for nuisance occurs.

- During working hours, technical staff will be available to monitor dust levels as appropriate; and
- At all times, the dust management procedures put in place will be strictly monitored and assessed.

The dust minimisation measures should be reviewed at regular intervals during the construction phase to ensure the effectiveness of the procedures in place and to maintain the goal of minimisation of dust generation. In the event of dust nuisance occurring outside the site boundary, site activities should be reviewed, and procedures implemented to rectify the problem. Specific dust control measures to be employed are presented below.

Site Routes

Site access routes (particularly unpaved areas) can be a significant source of fugitive dust from construction sites if control measures are not in place. The most effective means of suppressing dust emissions from unpaved roads is to apply speed restrictions. Studies show that these measures can have a control efficiency ranging from 25% to 80% ¹².

- A speed restriction of 20 km/hr will be applied as an effective control measure for dust for on-site vehicles or delivery vehicles within the vicinity of the site;
- Bowsers will be available during periods of dry weather throughout the construction period. Research shown found that the effect of surface watering is to reduce dust emissions by 50%. The bowser will operate during dry periods to ensure that unpaved areas are kept moist. The required application frequency will vary according to soil type, weather conditions and vehicular use; and
- Any hard surface roads will be swept to remove mud and aggregate materials from their surface while any unsurfaced areas shall be restricted to essential site traffic only.

Excavation

Excavation works during periods of high winds and dry weather conditions can be a significant source of dust.

- During dry and windy periods, and when there is a likelihood of dust nuisance, watering shall be conducted to ensure moisture content of materials being moved is high enough to increase the stability of the soil and thus suppress dust;
- During periods of very high winds (gales), activities likely to generate significant dust emissions should be postponed until the gale has subsided.

The movement of truck containing materials with a potential for dust generation to an off-site location will be enclosed or covered.

Stockpiling

The location and moisture content of stockpiles are important factors which determine their potential for dust emissions. The following measures will be put in place:

- Overburden material will be protected from exposure to wind by storing the material in sheltered parts of the site, where possible;
- Regular watering will take place during dry/windy periods to ensure the moisture content is high enough to increase the stability of the soil and suppress dust

Site Traffic on Public Roads

Spillage and blow-off of debris, aggregates and fine material onto public roads will be reduced to a minimum by employing the following measures:

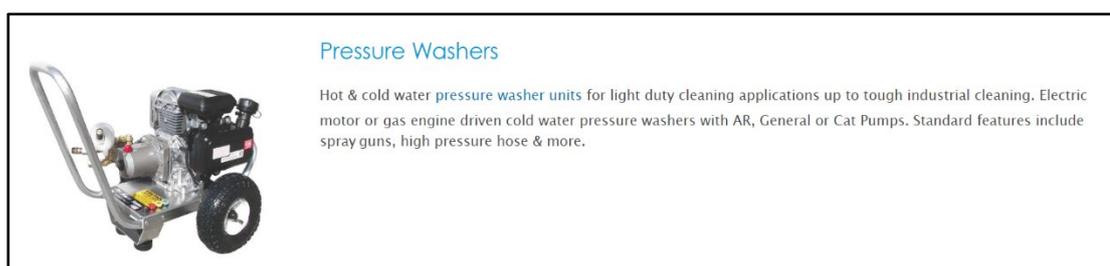


Figure 7.1 Example of Proposed wheel cleaning equipment example

- Vehicles delivering material with potential for dust emissions to an off-site location shall be enclosed or covered at all times to restrict the escape of dust;
- Any hard surface site roads will be swept to remove mud and aggregate materials from their surface while any unsurfaced roads shall be restricted to essential site traffic only.
- A power washing facility or wheel cleaning facility will be installed near to the site compound for use by vehicles exiting the site when appropriate, and an example of the washing equipment can be seen in insert 7.1 ; and
- Road sweepers will be employed to clean the site access route as required.

General

The pro-active control of fugitive dust will ensure that the prevention of significant emissions, rather than an inefficient attempt to control them once they have been released, will contribute towards the satisfactory management of dust by the construction contractor.

7.3 Ecology

The key strategies to be undertaken to minimise impact on the local flora and fauna during site clearing and construction are as follows:

- All site clearance works will comply with current legislative requirements and best practice;
- Taking measures to limit the working area during the construction phase will reduce the impacts of the development on adjacent areas. The construction area will be clearly delimited by the site boundary and machinery should operate only within this allocated site area;
- All re-fuelling of plant, equipment and vehicles will be carried out at the construction site boundary. All fuels, chemicals, liquid and solid waste will be stored in areas bunded in accordance with established best practice guidelines at the construction compound also; and Provision of spill kits;
- Provision of a water and sediment management plan, providing for means to ensure that surface water run-off is controlled such that no silt or other pollutants enter local water courses or drains; and
- The measures outlined in Section 7.6 will ensure that silt run-off and potential flooding risks are minimised which will protect any ecological receptors associated with the site.
- Construction lighting will be designed so as to be sensitive to the potential presence of bats and should adhere to the following guidance:
 - Bats & Lighting: Guidance Notes for Planners, engineers, architects and developers (Bat Conservation Trust, 2010) ¹³;
 - Guidance Notes for the Reduction of Obtrusive Light GN01 (Institute of Lighting Professionals, 2011) ¹⁴;
 - Bats and Artificial Lighting in the UK – Bats and the Built Environment Series. Guidance Note 08/18 (Bat Conservation Trust UK, 2018) ¹⁵.

7.4 Noise and Vibration

Noise impacts arising from construction activities have the potential to cause annoyance or nuisance to local residents and businesses in the area.

Appropriate criteria relating to permissible construction noise levels for this development are taken from British Standard BS 5228 – 1: 2009 +A1 2014¹⁶: Code of Practice for Noise and Vibration Control on Construction and Open Sites – Noise. The approach adopted here calls for the designation of a noise sensitive location into a

specific category (A, B or C) based on existing ambient noise levels in the absence of construction noise.

In accordance with the standard, ambient measured noise levels representative of noise sensitive locations should be rounded to the nearest 5 dB and construction noise limits are then set according to the category definitions above. This then sets a threshold noise value that, if exceeded at this location, indicates a potential significant noise impact is associated with the construction activities depending on context. The approach is summarised in Table 7.1.

Table 7.1: Threshold of Potential Significant Effect at Dwellings (BS5228-1)

Assessment Category and Threshold Value Period	Threshold Value (dB)		
	Category A ^{A)}	Category B ^{B)}	Category C ^{C)}
Night Time (23:00-07:00)	45	50	55
Evenings and Weekends ^{D)}	55	60	65
Daytime (07:00-19:00) and Saturdays (07:00 – 13:00)	65	70	75

- A) Category A: threshold values to use when ambient noise levels (when rounded to the nearest 5 dB) are less than these values.
- B) Category B: threshold values to use when ambient noise levels (when rounded to the nearest 5 dB) are the same as category A values.
- C) Category C: threshold values to use when ambient noise levels (when rounded to the nearest 5 dB) are higher than category A values.
- D) 19:00–23:00 weekdays, 13:00–23:00 Saturdays and 07:00–23:00 Sundays.

7.4.2 Vibration Criteria

Vibration criteria are taken from BS 5228-2:2009+A1:2014 Code of Practice for Noise and Vibration Control on Construction and Open Sites- Vibration. This document sets the following vibration limits for transient vibration. For buildings or structures that are structurally unsound, lower vibration magnitudes will apply, typically 50% of those for structurally sound buildings. Protected or historic buildings are not automatically assumed to be more vulnerable to vibration unless they have existing structural defects. The recommend transient vibration thresholds from BS5228-2 for the avoidance of cosmetic damage to light and heavy framed buildings are summarised in Table 7.2.

Table 7.2: *Transient Vibration threshold values for buildings*

Type of Building	Peak component particle velocity in frequency range of predominant pulse <small>Note 1</small>	
	4 Hz to 15 Hz	15 Hz and above
Reinforced or framed structures. Industrial and heavy commercial buildings	50mm/s	
Unreinforced or light framed structures. Residential or light commercial buildings.	15 mm/s at 4 Hz ^{Note 2} increasing to 20 mm/s at 15 Hz	20 mm/s at 15 Hz increasing to 50 mm/s at 40 Hz and above

Note 1: Values referred to are at the base of the building.

Note 2: At frequencies below 4 Hz, a maximum displacement of 0.6 mm (zero to peak) is not to be exceeded.

Human response to vibration stimuli occurs at orders of magnitudes below those associated with any form of building damage, hence vibration levels lower than those indicated in Table 7.2 can lead to concern. BS5228-2 also provides a useful guide relating to the assessment of human response to vibration in terms of PPV. Whilst the guide values are commonly used to compare typical human response to construction works, they tend to relate closely to general levels of vibration perception from other general sources. Table 7.3 below summarises the range of vibration values and the associated potential effects on humans.

Vibration Level, PPV	Effect
0.14 mm/s	Vibration might be just perceptible in the most sensitive situations for most vibration frequencies. At lower frequencies people are less sensitive to vibration.
0.3 mm/s	Vibration might be just perceptible in residential environments.
1 mm/s	It is likely that a vibration level of this magnitude in residential environments will cause complaint.

Table 7.3 Guidance on Effects of Human Response to PPV Magnitudes

7.4.3 General Noise and Vibration Mitigation

Best practice noise and vibration control measures will be employed by the contractor during the construction phase in order to control noise and vibration impacts at the nearest noise sensitive locations. All works on site shall comply with BS 5228 2009+ A1 2014 (Parts 1 & 2) which gives detailed guidance on the control of noise and vibration from construction activities. This includes guidance on several aspects of construction site mitigation measures, including, but not limited to:

- Selection of quiet plant;
- Noise control at source;
- Screening, and;
- Liaison with the Public

The following key forms of noise control for the site are set out below:

- Site compounds will be located away from noise sensitive boundaries within the site constraints;

- For mobile plant items such as cranes, dump trucks, excavators and loaders, the installation of an acoustic exhaust and or maintaining enclosure panels closed during operation can reduce noise levels by up to 10dB. Mobile plant should be switched off when not in use and not left idling.
- For steady continuous noise, such as that generated by diesel engines, it may be possible to reduce the noise emitted by fitting a more effective exhaust silencer system and avoid idling of engines when not in use.
- For percussive tools, a number of noise control measures include fitting a muffler or sound reducing equipment to the breaker 'tool' and ensure any leaks in the air lines are sealed. Erection of localised screens around breaker or drill bit when in operation in close proximity to noise sensitive boundaries.
- The use of a high-quality construction site hoarding will be included around all noise sensitive boundaries.
- For all materials handling, ensure that materials are not dropped from excessive heights, lining drops chutes and dump trucks with resilient materials.
- All items of plant should be subject to regular maintenance. Such maintenance can prevent unnecessary increases in plant noise and can serve to prolong the effectiveness of noise control measures.
- All site staff shall be briefed on noise mitigation measures and the application of best practicable means to be employed to control noise.

Liaison with the Public

The designated environmental liaison officer will be appointed to site during construction works. Any noise complaints will be logged and followed up in a prompt fashion by the liaison officer. In addition, where a particularly noisy construction activity is planned or other works with the potential to generate high levels of noise, or where noisy works are expected to operate outside of normal working hours etc., the liaison officer will inform the nearest noise sensitive locations of the time and expected duration of the noisy works.

Any noise complaints related to activities at the site will be logged and investigated and, where required, measures taken to ameliorate the source of the noise complaint.

Monitoring

During the construction phase, spot check noise monitoring may be required where the construction noise thresholds have the potential to be exceeded at noise sensitive locations. The monitoring shall be carried out by the contractor and used to inform the requirement for any control measures on site to reduce construction noise levels.

Noise monitoring will be conducted in accordance with the International Standard ISO 1996-2:2017 - *Description, measurement and assessment of environmental noise - Part 2: Determination of sound pressure levels* (ISO 2017)¹⁷.

Where required, or requested by the local authority, unattended external noise monitoring will be undertaken at locations on the site boundary closest to sensitive locations. It is considered that it will be appropriate to amend the monitoring program and location as the works progress. Accordingly, monitors may be added, removed or relocated as necessary.

The noise monitoring terminals should provide the following at minimum:

- Logging at hourly intervals; and

- Remote access for information download.

Where required (i.e. where there is potential for exceedance of the vibration thresholds for buildings in Table 7.2), or requested by the local authority, vibration monitoring will be installed at the site boundary to monitor Peak Particle Velocity parameter (PPV, mm/s) in the X, Y and Z directions, in accordance with BS ISO 4866: 2010: *Mechanical vibration and shock – Vibration of fixed structures – Guidelines for the measurement of vibrations and evaluation of their effects on structures*¹⁸.

The mounting of the transducer to the vibrating structure will need to comply with BS EN ISO 5348: 1998: *Mechanical vibration and shock – Mechanical mounting of accelerometers*¹⁹. In summary, the following ideal mounting conditions apply:

- The transducer and its mountings should be as rigid as possible;
- The mounting surfaces should be as clean and flat as possible;
- Simple symmetric mountings are best, and;
- The mass of the mounting should be small in comparison to that of the structure under test.

7.5 Resource and Waste Management

This section outlines the measures that will be undertaken to minimise the quantity of waste produced at the site and the measures to handle the waste in such a manner as to minimise the effects on the environment. A site-specific RWMP has been prepared by AWN Consulting and will be employed to ensure sustainable and effective waste management throughout the demolition, excavation and construction phases of the project.

Adherence to the RWMP prepared for the construction & demolition works will ensure that the management of waste arising is dealt with in compliance with the provisions of the *Waste Management Act 1996* as amended²⁰, associated Regulations, the *Litter Pollution Act of 1997* as amended²¹ and the *Eastern-Midlands Region Waste Management Plan 2015 – 2021*²² and the *National Waste Management Plan for a Circular Economy (NWMPCE)*²³, and that it will achieve optimum levels of waste reduction, re-use and recycling.

Typical waste materials that will be generated from the construction works will include:

- Soil and stones;
- Concrete, bricks, tiles and ceramics;
- Wood, glass and plastics;
- Metals;
- Gypsum-based construction material;
- Paper and cardboard;
- Mixed construction and demolition (C&D) waste;
- Chemicals (solvents, paints, adhesives, detergents etc.); and

The management of all hazardous waste arisings, if they occur, shall be coordinated in liaison with Health and Safety Management.

7.5.1 Waste Minimisation

Waste minimisation measures proposed are summarised as follows (and are described in more detail in the RWMP):

- Materials will be ordered on an 'as needed' basis to prevent over supply;

- Materials will be correctly stored and handled to minimise the generation of damaged materials;
- Materials will be ordered in appropriate sequence to minimise materials stored on site;
- A waste tracking log will be established;
- Sub-contractors will be responsible for similarly managing their wastes; and
- All wood waste generated by site works will be inspected and examined and will be segregated as re-useable wood and scrap wood waste.

7.5.2 Waste Storage

The main waste storage area will be located in the site compound. A dedicated and secure area containing bins, and/or skips, and storage areas, into which all waste materials generated by construction site activities, will be established within the development (see Figure 3.1).

Waste materials generated will be segregated on at the site compound, where it is practical. Where the on-site segregation of certain wastes types is not practical, off-site segregation will be carried out. There will be skips and receptacles provided to facilitate segregation at source. All waste receptacles leaving site will be covered or enclosed. The appointed waste contractor will collect and transfer the wastes as receptacles are filled. There are numerous waste contractors in the Dublin Region that provide this service.

The site Resource Manager will ensure that all staff are informed of the requirements for segregation of waste materials by means of clear signage and verbal instruction. Appointed employees will be made responsible for ensuring good site housekeeping.

7.5.3 Pest Management

A pest control operator will be appointed as required to manage pest onsite during the construction phase of the project. Organic and food wastes generated by staff will not be stored in open skips, but in closed waste receptacles. Any waste receptacles will be carefully managed to prevent leaks, odours and pest problems.

7.5.4 Responsibility

It will be the responsibility of the construction manager to ensure that a written record of all quantities and natures of wastes removed from the site are maintained on-site in a waste file (in hardcopy or electronically).

It is the responsibility of the project manager or his/her delegate that all contracted waste haulage drivers hold an appropriate waste collection permit for the transport of waste loads and that all waste materials are delivered to an appropriately licensed or permitted waste facility in compliance with the relevant Regulations as outlined in the RWMP.

The contractor, as part of regular site inspection audits, will determine the effectiveness of the waste management strategy and will assist the project manager in implementing the measures under the RWMP and in determining the best methods for waste minimisation, reduction, re-use, recycling and disposal as the construction phase progresses and waste materials are generated.

Prior to commencement of the demolition, excavation and construction activity and removal of any waste off-site, details of the proposed destination of each waste stream will be provided to FCC, along with waste collection permit numbers.

7.6 Surface Water Management

Run-off into excavations/earthworks cannot be prevented entirely and is largely a function of prevailing weather conditions.

Care will be taken to ensure that exposed soil surfaces are stable to minimise erosion. All exposed soil surfaces will be within the main excavation site which limits the potential for any offsite impacts. All run-off will be prevented from directly entering into any water courses as no construction will be undertaken directly adjacent to open water.

No significant dewatering will be required during the construction phase which would result in the localised lowering of the water table. There may be localised pumping of surface run-off from the excavations during and after heavy rainfall events to ensure that the excavation is kept relatively dry.

The following measures will be put in place during the construction phase to ensure protection of surface waterbodies. Construction works are informed by best practice guidance from Inland Fisheries Ireland on the prevention of pollution during development projects:

- Control of Water Pollution from construction Sites, Guidance for consultants and contractors (C532); and
- Guidelines on Protection of Fisheries During Construction Works in and Adjacent to Waters (2016).
- Environmental Good Practice on Site (3rd edition) (C692).

Surface water discharge from the site will be managed and controlled for the duration of the construction works until the permanently attenuated surface water drainage system of the proposed site is complete. A temporary drainage system shall be installed prior to the commencement of the construction works to collect surface water runoff by the site during construction.

It is envisaged that a number of geotextile lined settling basins and temporary mounding's and/or silt fences will be installed to ensure silts do not flow off site during the construction stage. This temporary surface water management facility will throttle runoff and allow suspended solids to be settled out and removed. All inlets to the settling basins will be 'riprapped' to prevent scour and erosion in the vicinity of the inlet.

7.6.1 Pollution Control

Management of Suspended solids in run-off

Any temporary storage of spoil, hardcore, crushed concrete or similar material will be stored as far as possible from any surface water drains and also stored in receptacles where possible. In order to minimise the risk of contamination, the stockpiled material will be removed off-site as soon as possible. Surface water drain gratings in areas near or close to where stockpiles are located will be covered by appropriate durable polyurethane covers or similar.

There will be no direct pumping of silty water from the works to any watercourse. Sediment entrapment facilities will be installed to reduce sediment discharges to downstream properties and receiving waters. All run-off leaving a disturbed area will pass through a sediment entrapment facility before it exits the site and flows downstream such as straw bales, silt fencing, silt barriers and diversion dams.

Concrete Run-off

No wash-down or wash-out of ready-mix concrete vehicles during the construction works will be carried out at the site within 10 meters of an existing surface water drainage point. Wash-outs will only be allowed to take place in designated areas with an impervious surface.

Accidental Spills and Leaks

No bulk chemicals will be stored within the active construction areas. Temporary oil and fuel storage tanks will be kept in the material storage area in suitable containers and will be appropriately bunded as required. Refuelling of vehicles and the addition of hydraulic oils or lubricants to vehicles will take place in designated areas of the site, where possible, which will be kept away from surface water drains.

Spill protection equipment such as absorbent mats, socks and sand will be available to be used in the event of an accidental release during refuelling. Training will be given to appropriate site workers in how to manage a spill event.

The following mitigation measures will be taken at the construction site in order to prevent any spillages to ground of fuels during machinery activities and prevent any resulting soil and/or groundwater quality impacts:

- Refuelling will be undertaken off site where possible;
- Where mobile fuel bowsers are used the following measures will be taken:
 - Any flexible pipe, tap or valve will be fitted with a lock and will be secured when not in use;
 - The pump or valve will be fitted with a lock and will be secured when not in use;
 - All bowsers must carry a spill kit;
 - Operatives must have spill response training; and
 - Portable generators or similar fuel containing equipment will be placed on suitable drip trays.

Monitoring

Weekly checks will be carried out to ensure surface water drains are not blocked by silt, or other items, and that all storage is located at least 10m from surface water receptors. A regular log of inspections will be maintained, and any significant blockage or spill incidents will be recorded for root cause investigation purposes and updating procedures to ensure incidents do not reoccur.

8.0 SUMMARY

This CEMP sets out the overall management strategy for demolition, excavation and construction works for the proposed development. The CEMP aims to ensure the management of construction activity is carried out in a planned, structured and considerate manner which minimises the impacts of the works on the local environment, residents and commercial activities in the vicinity of the site. Due to the nature of construction works, there may be unforeseen events which occur at the site and the project team will actively manage any changes and discuss with the relevant authorities, where required.

The CEMP will be reviewed regularly and will be updated by the construction contractor to account for any subsequent planning conditions issued, any updated guidance released and circumstantial changes at the site as the development progresses.

The project team are committed to ensuring that the construction activities to be carried out are pro-actively managed so as to minimise potential impacts.

9.0 REFERENCES

1. Environmental Protection Agency (EPA) '*Best Practice Guidelines for the Preparation of Resource and Waste Management Plans for Construction & Demolition Projects*' (2021).
2. Environmental Protection Agency (EPA), *Waste Classification: List of Waste & Determining if Waste is Hazardous or Non-Hazardous* (2015)
3. Council Decision 2003/33/EC, establishing criteria and procedures for the acceptance of waste at landfills pursuant to Article 16 of and Annex II to Directive 1999/31/EC.
4. British Standards Institution (BSI), *BS EN 1992-3:2006 Eurocode 2: Design of concrete structures. Liquid retaining and containment structures*. (2006).
5. Department of Transport, *Traffic Signs Manual 2010 – Chapter 8 Temporary Traffic Measures and Signs for Roadworks* (2010).
6. Department of Transport, *Guidance for the Control and Management of Traffic at Road Works* (2010).
7. Department of Transport, Tourism and Sport and Department of Housing, Planning and Local Government, *Design Manual for Urban Roads and Streets* (2019).
8. Department of Environment, Heritage and Local Government (DOEHLG), *Quarries and Ancillary Activities, Guidelines for Planning Authorities* (2004).
9. US Environment Protection Agency (USEPA), *Compilation of Air Pollutant Emission Factors, AP-42, Fifth Edition (periodically updated)* (1986).
10. The Scottish Office – Development Department, *Planning Advice Note PAN50 Controlling the Environmental Effects Of Surface Mineral Workings Annex B: The Control of Dust at Surface Mineral Workings* (1996).
11. Institute of Air Quality Management (IAQM), *Guidance on the Assessment of Dust from Demolition and Construction* (2014).
12. USEPA, *Fugitive Dust Technical Information Document for the Best Available Control Measures* (1997).
13. Bat Conservation Trust, *Bats & Lighting: Guidance Notes for Planners, engineers, architects and developers* (2018).
14. Institute of Lighting Professionals, *Guidance Notes for the Reduction of Obtrusive Light GN01* (2011).
15. Bat Conservation Trust UK, *Bats and Lighting in the UK – Bats and the Built Environment Series* (2008).
16. British Standards Institution (BSI), *BS 5228-2:2009 Code of practice for noise and vibration control on construction and open sites. Vibration (+A1:2014)* (2009).
17. International Standard ISO 1996-2:2017 - Description, measurement and assessment of environmental noise - Part 2: Determination of sound pressure levels (ISO 2017).
18. British Standards Institution (BSI), *BS ISO 4866: 2010: Mechanical vibration and shock – Vibration of fixed structures – Guidelines for the measurement of vibrations and evaluation of their effects on structures* (2010).
19. British Standards Institution (BSI), *BS EN ISO 5348: 1998: Mechanical vibration and shock – Mechanical mounting of accelerometers* (1998).
20. *Waste Management Act 1996* (No. 10 of 1996) as amended, including sub-ordinate and associated legislation.
21. *Litter Pollution Act 1997* (No. 12 of 1997) as amended
22. Regional Waste Management Planning Offices, *The National Waste Management Plan for a Circular Economy 2024 - 2030* (2024).
